


**U.S. DEPARTMENT OF THE INTERIOR – BUREAU OF LAND MANAGEMENT  
RADIO FACILITY CONSTRUCTION AND REMEDIATION  
BID PACKAGE 2: ARCATA AND UKIAH FIELD OFFICES**

**RADIO FACILITY CONSTRUCTION SPECIFICATIONS**

Three radio facilities are included in this Construction Bid Package:

Cahto Peak  
Cooskie Mountain  
Walker Ridge

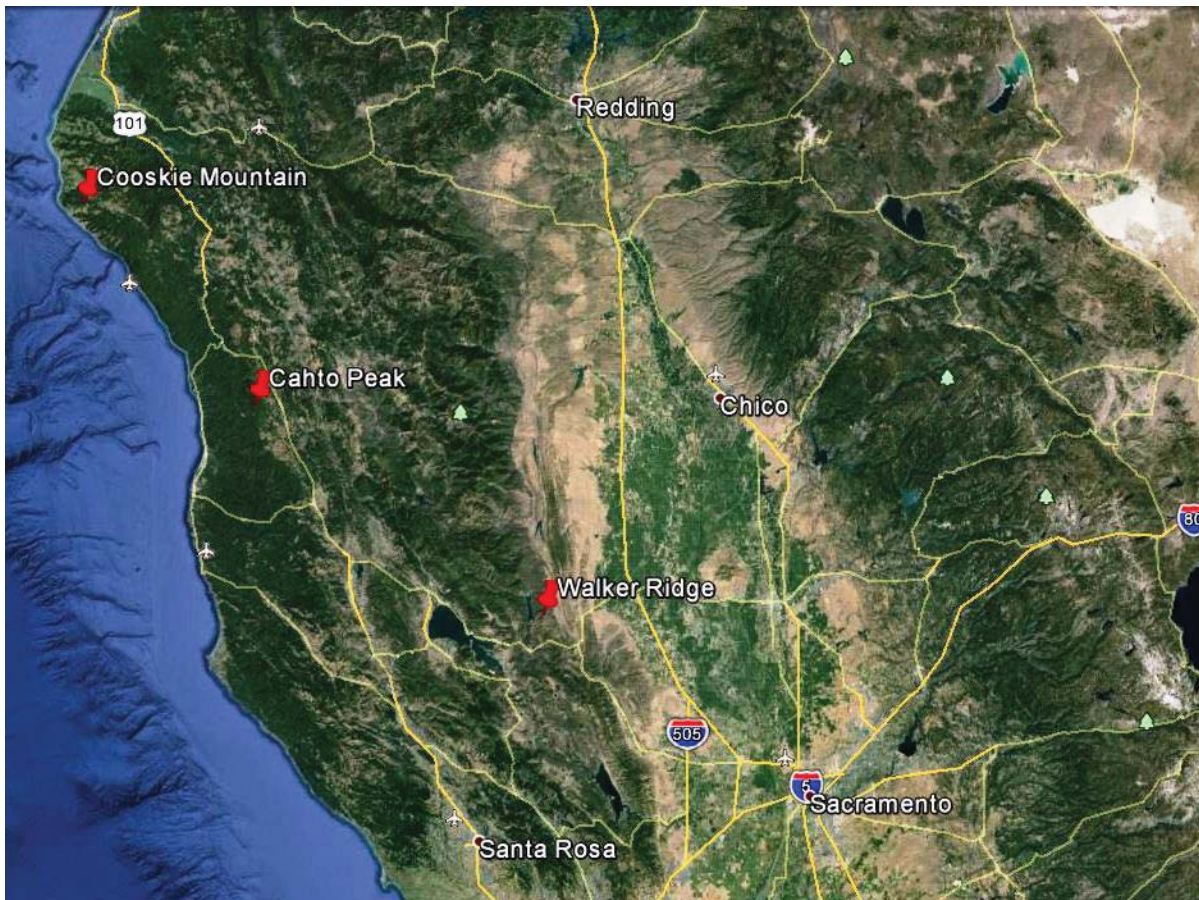

**U.S. DEPARTMENT OF THE INTERIOR – BUREAU OF LAND MANAGEMENT**  
**RADIO FACILITY CONSTRUCTION AND REMEDIATION**  
**BID PACKAGE 2: ARCATA AND UKIAH FIELD OFFICES**

**TABLE OF CONTENTS**

Table of Contents .....	2
<u>Division 01 - General Requirements</u> .....	4
Section 01 00 00 – General Requirements .....	4
1.1 Related Documents.....	4
1.2 Summary of Work.....	4
1.3 Technical Information to be submitted with Proposal.....	4
1.4 Section 01 31 00 - Project Management and Coordination.....	5
1.5 Section 01 33 00 – Submittal Procedures .....	5
1.6 Section 01 42 00 – Reference Standards and Definitions.....	7
1.7 Section 01 50 00 – Temporary Facilities .....	9
2.1 Section 01 60 00 – Product Requirements.....	10
3.1 Section 01 70 00 – Execution Requirements .....	11
3.2. Contractor responsibilities.....	13
3.3 Submittal Data and Notification Requirements.....	14
3.4 civil development .....	14
Cahto Peak – Section 01 11 00 – Summary of Work.....	15
PART 1: General.....	16
PART 2: Products .....	20
PART 3: Execution.....	30
PART 4: Cahto Peak – Drawings .....	43
PART 5: Cahto Peak – Contractor Bid Document.....	44
Cooskie Mountain – Section 01 11 00 – Summary of Work.....	50
PART 1: General.....	51
PART 2: Products .....	54
PART 3: Execution.....	57
PART 4: Cooskie Mountain – Drawings .....	64
PART 5: Cooskie Mountain – Contractor Bid Document.....	65
Walker Ridge – Section 01 11 00 – Summary of Work .....	68
PART 1: General.....	69
PART 2: Products .....	72
PART 3: Execution.....	83
PART 4: Walker Ridge – Drawings.....	96
PART 5: Walker Ridge – Contractor Bid Document .....	97
Section 01 11 00 – Typical Design Drawings .....	102
Section 01 45 23 – Third-Party Testing and Inspection Services.....	103
Section 01 77 00 – Contract Closeout Requirements .....	130
Section 01 78 39.13 – Project Record Documents.....	135
Division 02 – Existing Conditions.....	139
Section 02 21 00 – Site Surveys .....	139
Section 02 41 16 – Structure Demolition .....	143
Section 02 41 19 – Selective Demolition .....	150
Division 13 - Special Construction.....	157
Section 13 34 18 – PreFabricated Communications Shelter.....	157
Section 13 34 23 – Prefabricated Shelter Foundation.....	168
<u>Division 23 - Heating, Ventilating, and Air Conditioning</u> .....	175
Section 23 00 01 – Heating, Ventilation and Air Conditioning (HVAC) .....	175
Division 26 - Electrical .....	178
Section 26 05 00 – Basic Electrical Materials and Methods.....	178
Section 26 21 13 – Low-Voltage Electrical Service-Entrance .....	183
Section 26 24 16 – Panel Boards .....	187
Section 26 27 13 – Electricity Metering .....	192
Section 26 31 00 – Photovoltaic Collector System.....	196

**U.S. DEPARTMENT OF THE INTERIOR – BUREAU OF LAND MANAGEMENT  
RADIO FACILITY CONSTRUCTION AND REMEDIATION  
BID PACKAGE 2: ARCATA AND UKIAH FIELD OFFICES**

Section 26 33 01 – Battery Systems .....	206
Section 26 43 13 – Surge Protection Devices .....	214
Section 26 50 00 – Lighting .....	221
Division 27 - Communications .....	230
Section 27 05 10 – Cable and Wire Installation.....	230
Section 27 11 16 – Equipment Racks.....	248
Section 27 11 16.13 – Equipment Cabinet and Rack Installation .....	250
Section 27 11 16.20 – Equipment Installation in Racks and Cabinets .....	256
Division 31 – Earthwork .....	261
Section 31 10 00 – Site Clearing .....	261
Section 31 20 00 – Earthwork-Grading.....	262
Section 31 23 16 – Excavation and Fill.....	266
Section 31 23 17 – Trenching.....	272
Section 31 23 23 – Utility Backfill Materials .....	277
Division 32 – Exterior Improvements.....	283
Section 32 31 13 – Chain-Link Fences and Gates .....	283
Division 33 – Utilities and Grounding.....	287
Section 33 79 15 – Communications Shelter Grounding.....	287
Section 33 79 16 – Tower Grounding .....	290
Section 33 79 20 – Bonding Ancillary Devices to the External Grounding System.....	293
Section 33 79 83 – External Grounding Conductors .....	303
Section 33 79 83.13 – Grounding Electrodes .....	307
Section 33 79 83.20 – Supplemental Grounding Electrodes.....	312
Section 33 79 83.33 – Electrolytic Ground Rods.....	317
Section 33 79 83.53 – Grounding Electrode System Resistance.....	321
Section 33 79 83.63 – Special Grounding Situations .....	325
Section 33 79 84 – Internal Grounding and Bonding Conductors .....	329
Section 33 79 84.13 – Bonding Equipment to the Internal Grounding System .....	334
Section 33 79 84.16 – Rack Ground Bus Bar.....	340
Section 33 79 85 – Internal Perimeter Ground Bus.....	344
Section 33 79 86 – Ground Bus Bars at Remote Facilities .....	348
Section 33 81 13 – Communications Transmission Towers.....	355
Section 33 82 33.23 – RF Cable Ice Bridge .....	372
Section 33 83 13 – RF Cable Entrance Panels .....	376
